Charter School Project update: 13 October 2022

John Ryan, Programme Manager, Capital Projects, LBS Alison Harbottle, Head Teacher, Charter School



Department for Education





The Charter Schools Educational Trust









The Charter Schools Educational Trust

Chateau Building and Hall





Department for Education





The Charter Schools Educational Trust










The Charter Schools Educational Trust

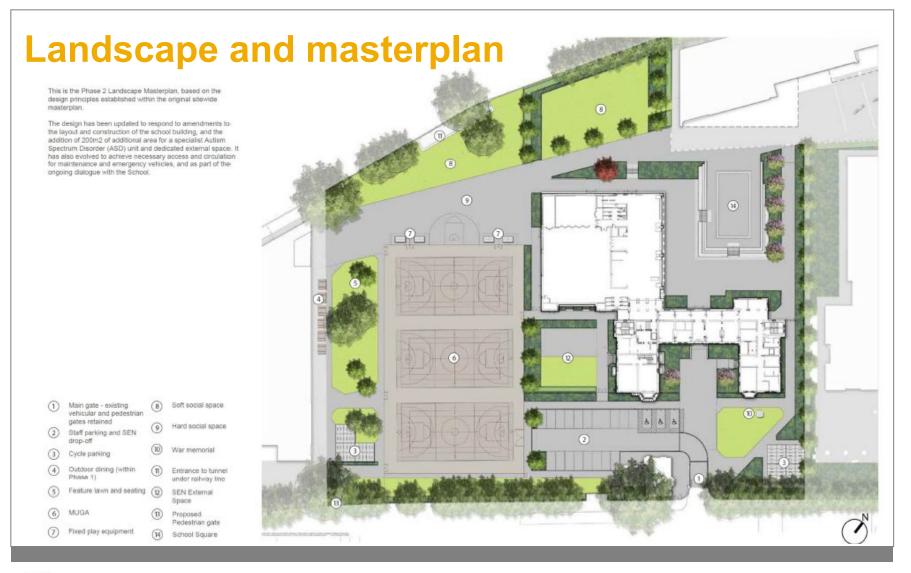







The Charter Schools Educational Trust









The Charter Schools Educational Trust

August 2023 Temporary Site Arrangement

Ko	
N e	y

Complete

	_	
1	1. Teaching Block	Nov 2018
	2. Dining and Sports Block	Nov 2018
	3. Existing Château Phase 2	
	4. Landscaping	Jan/Feb 2023
	5. MUGA	Oct 2021
	6. Phase 2 hoarding line	Mar 2023
	7 Temporary Accommodation	Aug 2023
	8 ASD Temporary Accommoda	tion Aug 2023

Phase 2 Construction Site Area



Department for Education





7.

5.

July 2024 Chateau and Hall complete

2.

(e	V

1.

Complete

1 Teaching Block	Nov 2018
2 Dining and Sports Block	Nov 2018
3 Chateau Phase 2	July 2024
4 Landscaping	Jan/Feb 2023
5 MUGA	Oct 2021
6 New Hall Phase 2	July 2024
7 Temporary Accommodation	Aug 2023
8 ASD Temporary Accommoda	ation Aug 2023



Department for Education



5.



August 2024 All work complete

2.

(0	V
	C	У

Complete

1 Teaching Block	
2 Dining and Sports Block	
3 Chateau Phase 2	
4 Landscaping	Jan
5 MUGA	
6 New Hall Phase 2	
7 Temps removed & landscap	oing

Nov 2018 Nov 2018 July 2024 an/Feb 2023 Oct 2021 July 2024 Aug 2024



Department for Education



5.



The Charter Schools Educational Trust
